

PRABANDH

BEYOND DELIVERY — REDEFINING PROJECT SUCCESS



Project
Management
Institute.
Gujarat, India

FROM THE EDITOR'S DESK



Mr. Mehulkumar Patel

Vice President - Marketing & Communication,
PMI Gujarat, India Chapter

Dear Readers,

Project success has long been defined by the classical triple constraint- scope, schedule, and cost.

Yet, as this edition of **PRABANDH** thoughtfully demonstrates, true success lies far beyond delivery. It lies in value creation, stakeholder trust, resilience under pressure, and the ability to convert uncertainty into opportunity.

Our Third Annual Conference, **ANANTAM 2025: Embrace Curiosity**, was not merely an event milestone but a reflection of our chapter's evolution. Celebrating five years of PMI Gujarat Chapter, it brought together over **350 industry leaders**, practitioners, academicians, and CXOs—each contributing to a shared dialogue on digital transformation, sustainability, and future-ready project leadership. The **behind-the-scenes** efforts of our PMO and volunteers further reaffirmed that disciplined execution and collaborative spirit are the backbone of impactful outcomes.

This edition shares our membership, programs, academic and volunteering initiatives. We have also covered two impactful stories in our Knowledge Corner, highlighting how **leadership, transparency, and strategic thinking** can transform **challenges into opportunities** in projects. Emphasizing that delivery is merely an output while value represents an outcome, we advocate for **aligning competence with character and processes with purpose**, making project management a strategic advantage. Last but not least, congratulations to all PMI Gujarat Chapter members who have completed their PMI certifications.

Together, let's redefine success.

Warm regards,

Mehulkumar Patel

Editor, **PRABANDH**

PMI Gujarat, India Chapter

Board for FY2026-27



Mr. Prerak Shah
President, PMI Gujarat,
India Chapter



Mr. Rajesh Panchal
Vice President -
Administration



Mr. Darshil Mistry
Vice President -
Finance



Mr. Mehulkumar Patel
Vice President -
Membership



Mr. Bharat Thakarar
Vice President -
Training &
Development



Mr. Brijesh Shah
Vice President -
Programs



Mr. Rajit Shah
Vice President -
Corporate Relations



Mr. Mahesh Panchal
Vice President -
Academics Affiliation



Ms. Hiral (Vyas) Dave
Vice President -
Volunteer
Development



Mr. Sandip Karia
Vice President -
Marketing &
Communication



Mr. Suketu Modi
Vice President -
Technology

CHAPTER HIGHLIGHTS

PMI Gujarat Chapter Annual Conference: ANANTAM 2025

Ahmedabad | 13 December 2025

350+ Industry Leaders | Celebrating 5 Years of PMI Gujarat Chapter



CONFERENCE OVERVIEW

PMI Gujarat Chapter hosted its Third Annual Conference at Shree Shakti Convention Centre, marking a significant milestone as the chapter celebrated its fifth anniversary.

The event introduced the new identity — **ANANTAM** — symbolising infinite possibilities in project management.

The conference brought together leaders, practitioners, academicians, and CXOs for a full day of knowledge exchange, recognition of best practices, and strategic dialogue.



Why Anantam?

Anantam represents infinity, symbolizing the limitless nature of project management across various industries and global reach. It highlights the depth and diversity of project management practices.



Chief Guest Address Shri Mamta Verma, IAS

Principal Secretary, Industries & Mines Department
She highlighted Gujarat's transformative industrial growth, referencing Dholera Smart City and Vibrant Gujarat, and emphasized disciplined project execution as the backbone of national development.



CHAPTER HIGHLIGHTS

PMIGJC Annual Conference - ANANTAM 2025



CONFERENCE HIGHLIGHTS

President **Mr. Prerak Shah** reviewed the chapter's five-year journey and outlined new ideas for 2025-26, such as three SIGs, a sustainability project, PMP Preparation Guidance Group, and technology adoption. Keynote speakers included **Mr. Sameer Sinha** (Savvy Group), Wing Commander **Ms. Jaya Tare**, and **Mr. Pranav Pandya** (Dev Information Tech Ltd). Panel discussions involved industry and CXO experts from companies like TCS, L&T, Gift City, LTIMindTree, and others, focusing on strategies for digital transformation and sustainability.

A special session by award-winning film director-producer **Mr. Abhishek Jain** addressed project management in the film industry. Conference Director **Mr. Suketu Modi** emphasized the importance of digital and sustainable project management and noted record participation of 350 industry experts.

PMI Gujarat Chapter thanked all speakers, attendees, volunteers, and partners for making "ANANTAM 2025" a successful event.





ANANTAM GLIMPSES

PMIGJC Annual Conference - ANANTAM 2025

Registration

The conference event began with arrival for delegates and registration process



Lamp Lighting: Kicking Off the Event

Inauguration of the Conference by our Chief Guest, Shri Mamta Verma, IAS, officially opened the conference with a prayer and the lighting of a lamp.

Opening Remarks

We began with opening remarks from PMIGJC President Mr. Prerak Shah, followed by addresses from PMI R11 Mentor Mr. Prassanna Sampathkumar and Chapter Engagement Manager, PMI South Asia Mr. Abhishek Sharma.





ANANTAM GLIMPSES

PMIGJC Annual Conference - ANANTAM 2025

Keynote Speaker

Mr. Sameer Sinha emphasised that achieving ESG goals requires collective societal action beyond government efforts to drive sustainable growth.



Special Talk

Wing Cdr. Ms. Jaya Tare delivered a special talk on project management in the space industry, highlighting key Government of India initiatives.

Expert Lecture

Mr. Pranav Pandya touch upon the impact of adopting digital technology on the project planning, execution and governance.



Networking Break





ANANTAM GLIMPSES

PMIGJC Annual Conference - ANANTAM 2025



Panel Dialogue

“Digital Evolution: Adapting New-Edge Technologies in Project Management”, truly embodying the conference theme

Wadhvani Foundation Case Study

Mr. Kedar Pandya presented a case study, highlighting how a simple outreach evolved into a strong, purpose-driven partnership aligned with conference’s vision.



Networking Lunch



Celebrity Guest Session

Mr. Abhishek Jain shared a unique perspective, drawing parallels between filmmaking and project management as a form of organised chaos.





ANANTAM GLIMPSES

PMIGJC Annual Conference - ANANTAM 2025

CXO Talks - Panel Dialogue

The CXO panel dialogue at delivered strategic leadership insights and real-world perspectives aligned with the conference theme.



Sponsor's Kiosk

5-year Celebration





FELICITATION & SPONSORS HIGHLIGHTS

PMIGJC Annual Conference - ANANTAM 2025

For excellence in Project Management & Governance

Construction & Infrastructure

- Multimedia Consultants
- M&B Engineering Ltd.
- Rajkamal Builders and Infrastructure Pvt. Ltd.

Pharma & Life Science

- Zydus Lifesciences Ltd.
- Amneal Pharmaceuticals
- Cadila Pharmaceuticals
- Sun Pharmaceutical Inds.

Services

- Vasant Group
- Sahaj Solar Pvt Ltd

Manufacturing

- Shivalik Global Products Pvt. Ltd.
- AIA Engineering Ltd.

Information Technology

- GATEWAY Technolabs
- Dev Information Technology Ltd.
- eInfochips (An Arrow Company)
- TCS

For Promoting Project Management in Curriculum

Academia

- L.D College of Engg. & Tech.
- Nirma University
- Parul University
- CEPT

For their contributions and strong support

Individuals

- YEYOON KIM
- GIRISH KADAM
- BHARAT BHAGAT
- DR. SANJAY BUCH

Organizations

- PMI MUMBAI CHAPTER
- DEVX CO-WORKING SPACES
- All Events
- GESIA



FELICITATION & SPONSORS HIGHLIGHTS

PMIGJC Annual Conference - ANANTAM 2025

Sponsored and supported by:

Title Partner



Wadhvani Foundation

Co-sponsors



Zoho Corporation Pvt. Ltd.



MOWEB Technologies Pvt. Ltd.



Gray Ice India Pvt. Ltd.

Souvenir Partners

Logo Partners



Bosch Rexroth India Private
Ltd.



PMPeople



Currie & Brown (India) Pvt. Ltd



ANANTAM - BEHIND THE SCENES



The Anantam PMO Kick-off commenced successfully in October 2025!

Creating an extraordinary event alongside the Conference Volunteers, October 2025 edition!



Gathering of the Conference Volunteers crew in November 2025!



Nailing down the perfect spot for our conference in late November 2025!





ANANTAM - BEHIND THE SCENES

A whirlwind of planning pow-wows and lunch rendezvous kicks off, with our conference volunteers bubbling over with excitement and elbow grease to make the PMIGJC 2025 conference an epic triumph!

If you're skeptical, take a moment to explore the sneak peeks presented below!





MEMBERSHIP EXCELLENCE: ENHANCING ENGAGEMENT AND MEMBER VALUE

Membership Journey: A Seamless End-to-End Experience

The PMI Gujarat Chapter has designed a streamlined and member-centric onboarding journey to ensure a smooth start for every new member. Our process focuses on clarity, accessibility, and meaningful engagement from the very first interaction.

Membership Benefits: Value that Drives Professional Growth



PMI Gujarat Chapter offers an extensive range of benefits designed to support continuous professional development, industry networking, and knowledge growth. These benefits help members enhance their competencies and stay aligned with global project management standards.

Key Benefits Overview

Learning & Certifications

Access to study groups, exam prep sessions, and guidance for PMI certifications.

Networking & Community

Opportunities to connect with professionals across industries through events and forums.

Career Enablement

Career guidance, leadership opportunities, and volunteer roles that build visibility and experience.

Knowledge Sharing

Webinars, expert talks, SIG discussions, and curated resources for ongoing learning.

Industry Collaboration


Engagement with stakeholders across IT, construction, engineering, finance, and more.

Member-Exclusive Events


Special access to chapter programs, townhalls, and recognition activities.



MEMBERSHIP EXCELLENCE: ENHANCING ENGAGEMENT AND MEMBER VALUE



NEW MEMBER TREND



ACTIVE MEMBER BY MONTH

Membership Insights: Trends Shaping Our Growth

Membership trends highlight a rapidly growing and engaged community. The chapter has experienced a strong surge in new members, especially in the last two years. A majority of our members hold globally recognized certifications, indicating a deep commitment to professional excellence.

Key Insights Snapshot



PMI Gujarat Chapter remains committed to driving value, fostering collaboration, and strengthening the professional journey of every member. Through focused initiatives, diverse programs, and a culture of inclusiveness, we continue to build a thriving and future-ready project management community.





RECENT PROGRAMS HIGHLIGHTS

September 2025 – February 2026

Providing Value Beyond Events — Impact & Member Engagement



Total Programs

4



Total Registrations

483



Total Attendees

242



Average Feedback

8.5/10

Adapting to Change: How to Position Yourself in the AI World

21 September 2025 | 100 Attendees

Speaker: Mr. Amitabh Singh

Lean Thinking For Project Excellence

9 November 2025 | 35 Attendees

Speaker: Mr. Indraraj Nakoom





RECENT PROGRAMS HIGHLIGHTS

September 2025 – February 2026

Harnessing Generative AI for Project Planning

11 January 2026 | 41 Attendees


**Speaker: Ms. Simone De Rie
Mr. Bas Nab**



PM Story Circle - War Stories and Wins

8 February 2026 | 66 Attendees

Speaker: Multiple members shared experiences

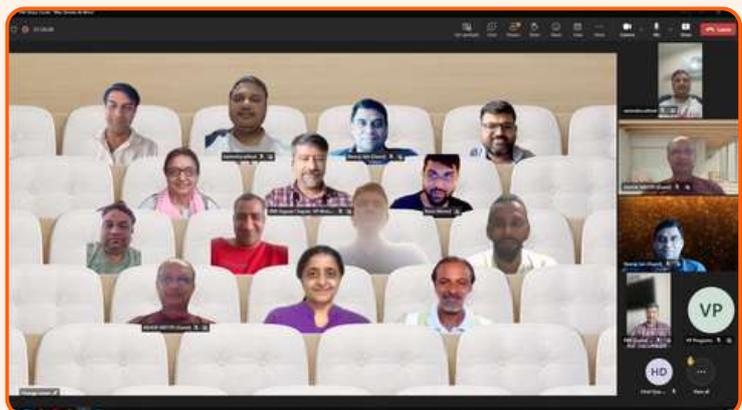

ACADEMICS & STUDENT ENGAGEMENT

From Classroom Concepts to Execution Excellence

Between November 2025 to February 2026



Institutions Engaged

LDCE, Nirma
University



185+

Students
Reached




3

Events
Conducted



Key Themes

AI | Career Strategy |
Crisis Simulation



VELOCITY: Escape the Gravity of the Classroom

LDCE | 6-7 February 2026 | 100+ Students

High-intensity, game-based event designed to move beyond theory into execution

- **HOSTILE TAKEOVER:**
 - Profit over peers
 - A strategic game where alliances collapse and only profit matters.
 - Outsmart competitors and seize control.
- **CAREER LADDER:**
 - From questions to conclusions
 - A game that challenges your knowledge of careers.
 - Navigate critical questions, make decisive calls.
- **THE PROJECT TRAITOR:**
 - Spot the liar
 - A psychological deduction game built on deception and trust.
 - Identify the imposter before the imposter takes your firm down.
- **THE PROJECT APOCALYPSE:**
 - A crisis-management game focused on chaos.
 - Restore order by analyzing limited information under pressure.



ACADEMICS & STUDENT ENGAGEMENT



AI AGENTS IN ACTION

LDCE | 29 November 2025 | 45+ Students

Automate Tasks, Boost Productivity,
Transform Marketing



AI IN PROJECT MANAGEMENT

Nirma | 1 November 2025 | 40+ Students

AI as a Catalyst for Project Excellence





VOLUNTEER ENGAGEMENT HIGHLIGHTS

September 2025 to March 2026

NEW VOLUNTEERING ORIENTATION (Virtual)

15 September 2025 | Online MS Teams

Focus Areas:

- Do's & Don'ts
- PMIGJC Overview
- Volunteer Journey Ahead




VOLUNTEER QUARTERLY MEET - Q2

12 August 2025 | In Person

- Quarterly update & strategic align
- Meet & Greet
- Club AGM day

30+ Total Attendees (BODs & Volunteer)

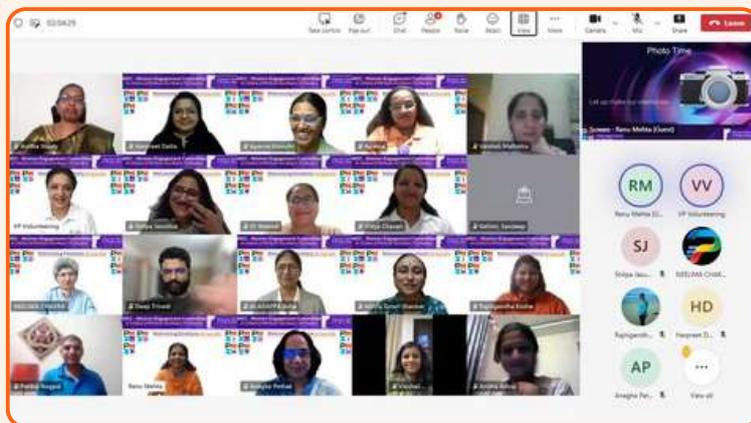

WEC EVENT 1 - WELCOMING EMOTION

6 September 2025 | Online MS Teams

240+ participants

- Supporting PMI's **#BeWelcoming** cultural and emotional intelligence



VOLUNTEER ENGAGEMENT HIGHLIGHTS

September 2025 to March 2026

ANANTAM 2025 - ANNUAL PMIGJC CONFERENCE

13 December 2025 | In Person

1500+ Hours	40+ Volunteer	19 PMO Member	10 Student Volunteer	300+ Attendees
-----------------------	-------------------------	-------------------------	--------------------------------	--------------------------

- **End-to-End support : Registration, Platform, PDU & Coordination**

WEC EVENT 2 - WELCOMING DIVERSITY

31 January 2026 | Online MS Teams

172+ Participants

Theme : **“Unlock Potential, Deliver Value”**

Support : Registration, Platform, PDU & Coordination



WEC IWD 2026 CELEBRATION - UPCOMING

15 March 2026 | Online

Theme : **Give to gain - Collaborate, Contribute, Celebrate!**

Work In Progress : Chapter Support Confirmed!



“ROLE OF TEAM WORK IN MITIGATING THE OPERATIONAL RISK”

First well drilling by IR-900-I Drilling Rig at ONGC Mehsana, Gujarat

INTRODUCTION

Ingersoll rand drilling rig was purchased by ONGC in 1985 for drilling oil wells from Ingersoll Rand, USA, and is briefly described as the IR900-1 rig. This rig was commissioned in the Mehsana field, and the 1st drilling well was being drilled. I was the rig engineer of this rig and was a member of the team who visited Hunston, USA, for brief training along with others. The drilling rig was assembled & commissioned by starting the drilling of the first well. The commissioning engineer from the manufacturer (OEM) and supplier of the rig left the site and went to another place after the successful start of drilling.

CHALLENGES FACED

The rig had two mud pump sets, each powered by one Caterpillar diesel engine. During operation, only one mud pump engine is required for pumping mud into the well. After some days, another engine was tested for operations, which was the standby engine, and it was found that the engine was getting shut off automatically after running a few minutes. The rig crew checked but failed to diagnose the defect and rectify it by checking the diesel fuel system. The opening of the engine was not permissible, as it would violate the warranty clause as per the contract with the supplier. The help from the base workshop and other crews was taken but failed to resolve the issue.





KNOWLEDGE CORNER - CASE STUDY

“ROLE OF TEAM WORK IN MITIGATING THE OPERATIONAL RISK”

First well drilling by IR-900-I Drilling Rig at ONGC Mehsana, Gujarat

The matter was raised to top management, as there was a **risk of serious operational issues** in case of any functional issue with only running one engine. The matter was conveyed to OEM for sending a service engineer, which was not possible due to the nonavailability of an engineer on an immediate basis. OEM said that it may take a month's time to depute an engineer, which was not acceptable to the operational team. Each day was passing with try something to rectify defect without success.

SOLUTIONS IMPLEMENTED

One of the diesel mechanics, Mr. Mistry, told me to permit opening the fuel injectors one by one of the defective engine to check for any defect. I sought permission from my immediate senior, which was denied due to a warranty issue.

Seeing the seriousness, I raised the issue with top project management, and a hectic discussion was held before permission was granted. The injectors were opened and checked by the ONGC crew, and a minor crack was found in one injector, which was replaced by a new one. The engine was started and **tested successfully**. It became available for operations, and the **risk of operational shutdown was mitigated**.

RESULTS AND LESSONS LEARNED

The risk of operational shutdown of the drilling ring in case of any technical issue with only running the mud pump engine was mitigated. The standby engine was made operational.


We **must listen to all team members and evaluate their suggestions** with a cool mind.



CASE STUDY BY

Mr. Udham Singh,

ex CGM(M), ONGC ME(Mech)





TURNING A PROJECT THREAT INTO A VALUE-DRIVEN OPPORTUNITY

INTRODUCTION

In today's project environment, **success goes beyond “on time, on budget, on scope.”** It is ultimately measured by value delivered to the customer, trust built during uncertainty, and the resilience of the team's response. This case study highlights how our team converted a critical supplier delay into a business opportunity, applying core project management competencies aligned with the **PMBOK® Guide – Eighth Edition** and its emphasis on value-driven decision-making.



PROJECT CONTEXT

We were executing a turnkey EPC substation project that included critical 132 kV Gas Insulated Switchgear (GIS) along with associated substation systems. The substation formed a vital interface to enable the customer's hydroelectric plant to generate 96 MW of clean energy, significantly supporting regional development and contributing to the organization's social responsibility objectives by powering surrounding communities. Midway through execution, however, a major supplier announced a substantial delay in delivering a critical component. The impact was immediate and significant: schedule disruption, risk to revenue realization at plant start-up, and potential loss of stakeholder confidence.

CHALLENGES FACED

Critical-path disruption: The delayed component directly affected commissioning and overall completion.

Business continuity risk: The customer's ability to realize revenue was at stake.

Stakeholder confidence: Trust risked erosion if we over-promised or delayed transparency.

Limited levers: Expediting options were exhausted; replacement sourcing wasn't practical within the required window.

This was a textbook threat with the potential to cascade into contractual stress, reputational damage, and missed outcomes.




TURNING A PROJECT THREAT INTO A VALUE-DRIVEN OPPORTUNITY

SOLUTIONS IMPLEMENTED

Guided by PMI's value-centric definition of project management—applying knowledge, skills, tools, and techniques to meet or exceed intended value—we reframed the challenge.

Transparent Communication: We deliberately chose honesty over deferral. We informed the customer about the delay, its root cause, and realistic implications. This built a foundation for joint problem-solving rather than defensive posturing.

Customer Need Discovery: Our discussions revealed the customer's core priority: enable early power export from the hydro plant, even if the final configuration arrives later.



Alternative, Value-Adding Design: We proposed a temporary installation that allowed partial energization, enabling the hydro station to start exporting power to the grid and supporting regional demand while reinforcing the project's social and economic value.

Stakeholder Alignment & Cadence: We set a transparent update rhythm with both supplier and customer, aligned acceptance criteria for the temporary setup, and defined a clean transition plan to the final state. This preserved trust and reduced uncertainty.


RESULTS AND LESSONS LEARNED

Threat Converted into Opportunity: The customer approved the interim solution and issued a new order to implement it, expanding scope and strengthening commercial engagement.

Business Continuity and Value Delivery: Timely energization allowed the hydro plant to deliver renewable power to the region, fulfilling operational goals and supporting community needs. This demonstrated that value can be delivered even under constraints.



TURNING A PROJECT THREAT INTO A VALUE-DRIVEN OPPORTUNITY



Trust and Relationship Strengthened: The customer formally recognized our candor, responsiveness, and leadership, which transformed initial frustration into appreciation.

Execution Discipline Preserved: The temporary setup was executed safely and efficiently, with a defined cutover plan to the final configuration—no gold plating, no scope creep, just value-focused pragmatism.

Reinforcing PMI's Perspective:

This experience affirmed that **effective and efficient project management** is a strategic competency within organizations. By emphasizing **value-driven decision-making** and **stakeholder satisfaction**, we achieved outcomes that met and, in effect, exceeded intended value—despite constraints.

CONCLUSION

This case exemplifies “**Beyond Delivery**” in practice: success isn't merely hitting dates—it's protecting business outcomes, building trust, and creating options when disruptions occur. By aligning with the **PMBOK® Guide – Eighth Edition** mindset, we transformed a severe supplier delay from a delivery risk into a **customer-centric** opportunity. The outcome—additional order, **accelerated value**, and written appreciation—underscores a simple truth: project management, done right, is leadership in action and a strategic advantage.



CASE STUDY BY

Mr. Bhuvan Bhatt,

Project Management Team Leader

New Certificate Holders

NEW PMP CERTIFICATION HOLDERS

Data as of Feb 1, 2026

Amit Japthapi	Mohammad Burhan Mir	SVaibhav Gundawar
Jigar Kumar Patel	Abdul Kalim Shaikh	Dineshkumar Devabhai Vagdoda
Naveen Bhokal	Kajal Christie	Chandrakant Sakhare
Dhruli Doshi	Vishnu Karunakaran Pillai	Ronak Mehta
Priesh Saxena	Nitin Singh Parihar	Uma Awasthi
Faraz Ghoury	Manishkumar Prasad	Dhawal Dagli
Fhaizaan Baseer	Kailash Kishorchadra Padshah	Anurag Mittal
Natarajan Swamynathan	Manoj Kumar Singh	Smit Thakkar
Nirav Bhatt	Ritesh Kumar Ladohia	Gajjar Manojkumar Bipinchandra
Srijesh Sreenivas	Sandip Shishangiya	Ketulkumar Parmar
Earnest Prakash	Khaleel Shaik	Arpitkumar Amrutlal Patel
Monish Shah	Mrushad Dhiren Desai	Sunil Acharya
Umesh Charki	Shubham Jain	Rozal Bhatia
Chetan Soni	Nikunj Vig	Javed Ahmed
Syed Shahabaaz Patel	Fagun Safi	Ragavendran Kaliyamoorthi
Deepu Francis	Shubham Shah	Hirenkumar Shah
Ronak Parmar	Viju Raghavan	Ankit Desai
Chandra Kant	Yogesh Bhatt	Abil Ajith
Achintya Sharma	Lalitkumar Oza	Sanik Shah
Ram Choudhary	Dhruvinkumar Bhatt	Kaushalkumar Shah
Ravinder Singh	Parth Vyas	Harshkumar Parekh

New Certificate Holders

NEW PMP CERTIFICATION HOLDERS

Data as of Feb 1, 2026

Hemang Jani	Shreya Kansara	Ambrose Premkumar
Ami Darshnik Patel	Paras Patel	Basit Manzoor
Manali Patel	Jaymin Chetankumar Patel	Abdul Kareem Shaik
Amit Kumar Solanki	Prashant Soni	Mounik Vyas
Ankita Soni	Tejas Belani	Vijay Nakrani
Garlapati Chandrasekhar	Sumesh C	Rahul Rathore
Ramesh Kumar Sharma	Waseem Ahmed Syed	Sourendu Tah
Atul Tyagi	Babu Singh	Syed Jaffrin Ali Mohamed
Rajesh Nedumkot	Vimesh Mehta	Arth Parikh
Faraz Khan	Jinoy Patel	Sourabh Singh Rajput
Jeetendra Singh	Nikhil Solanki	Brajesh Dixit
Pallavi Chelluri	Ahmed Ameer Chand Khan	Nachiket Nileshkumar
Jignesh V Trivedi	Vaibhav Singh	Brahmbhatt
Doshi Ashesh	Amey Shanbhag	Jayesh Bhanderi
Rameshanchadra	Seby Palatty Poullose	Imran Ghanchi
M. Thailakandi Purail	Mukesh Kumar	Shreyansh Sinha
Meghaba Barad	Palvinder Singh	Hardik Shah
Praveen Dwivedi	Dipesh Bhavsar	Hina Jaiswal
Hiren Pandya	Syed Fahad Buqhari	Rishi Lalchandani
Kowshar Mondal	Shreyas Gandhi	Ishwarlal Yadav
Gobinath Mahendran	Yash Gadale	Bhavya Buch
Mansi Vaghasia	Rishabh Shukla	Faisal Javid Shah

New Certificate Holders

NEW PMP CERTIFICATION HOLDERS

Data as of Feb 1, 2026

Ankit Nigam

Salaudeen Habibullah

Rohan Singh

Ujjwal Srivastava

Nihal Ahmed

Kunal Mehta

Jignesh Shah

Alwin Mathew

Vinaykumar Patel

Vikas Singh

Jeel Mehta

Elavarasan M

Jaydeep Pandya

Ankit Makwana

Dhananjay Gupta

Raj Singh Sindal

Akshay Jain

Bhaumik Limbachia

Jaykumar Belhekar

Vipin Mishra

Anshul Rathore

Ganesh Muthaiah

Sonu Kumar

Salman Husainy

Akangsha Chadha

Bharat Vaishnav

Aagam Shah

Akash Goyal

Bhaiya Lal Anjana

Sanket Goswami

Yogesh Deshmukh

Dharmrajsinh Rana

Rabindra Kumar Asthana

Mahmed Riyaz

Kashif Mohammad

Sundaram Mylswamy

Harsh Arora

Rashaad Momin

Niraliben Modi

Pragya Arora

Parashuram Lamani

Abhijit Gujarathi

Priyankkumar Patel

Vetrivel Murugan

Deepak Khurana

Sanjeet Kumar

Dishi Joshi

Chetankumar Patel

Lekharaj Konasani

Anoop Sharma

Hitesh Gondalia

Saumya Shah

Tabish Khan

Remya Narayanan

Karthik Srk

Abhay Dixit

Pritpal Rehshi

Gaurang Ganatra

Abi Lais Siddiqui

Suresh Suresh

Thakkar Vatsal Vinodchandra

Jyotsna Chhikara

Harshadkumar Patel

Jigar Dave

Kishore Myadam

Gajendra Singh Thakur

Ashutosh Sharma

New Certificate Holders

OTHER PMI CERTIFICATIONS HOLDERS

Data as of Feb 1, 2026

CAPM

- Stavan Shah
- Zalak Shah
- Prajakta Tamhane
- Goswami Kundan Puri
- Riddhi Bhatia

PMI-ACP

- Faraz Siddiqui
- Chintan Bhanushali

PMI-SP

- Sathishbabu Nallusamy

PMI-RMP

- Dheeraj Srivastava
- Sonu Kumar
- Jikku Rajan
- Ajay Kumar

CPMAI

- Rajesh Panchal
- Sanjava Kaileshkumar Khimabhai

PMI-CP

- Vinod Garg

PfMP

- Rahul Raina



Editorial Team



Mr. Mehulkumar Patel
VP, Marketing Portfolio



Ms. Dehuti Jani
Volunteer, Marketing



Ms. Dishu Joshi
Volunteer, Marketing



Mr. Umang Salot
Volunteer, Marketing



Mr. Keval Asher
Volunteer, Marketing





Registered Office:

C-201, 2nd Floor, The First,
B/h Keshav Baugh Party Plot,
Nr. Shivalik High-Street, Vastrapur,
Ahmedabad, Gujarat 380015

Visit us at:

